


HARD WEST  
A-643


Initially "Liberty Hill  
Drive"

R023011 R023012  
NEIL CARROLL, et al  
895/553  
90.0 AC 3.001 AC

Bold dash lines  
indicate proposed  
lines of division  
to divide Mr. Campbell's  
33.79 ac. into 3  
11.25 ac tracts

RECORDERS MEMORANDUM  
All or parts of the text on this page was not  
clearly legible for satisfactory recordation.

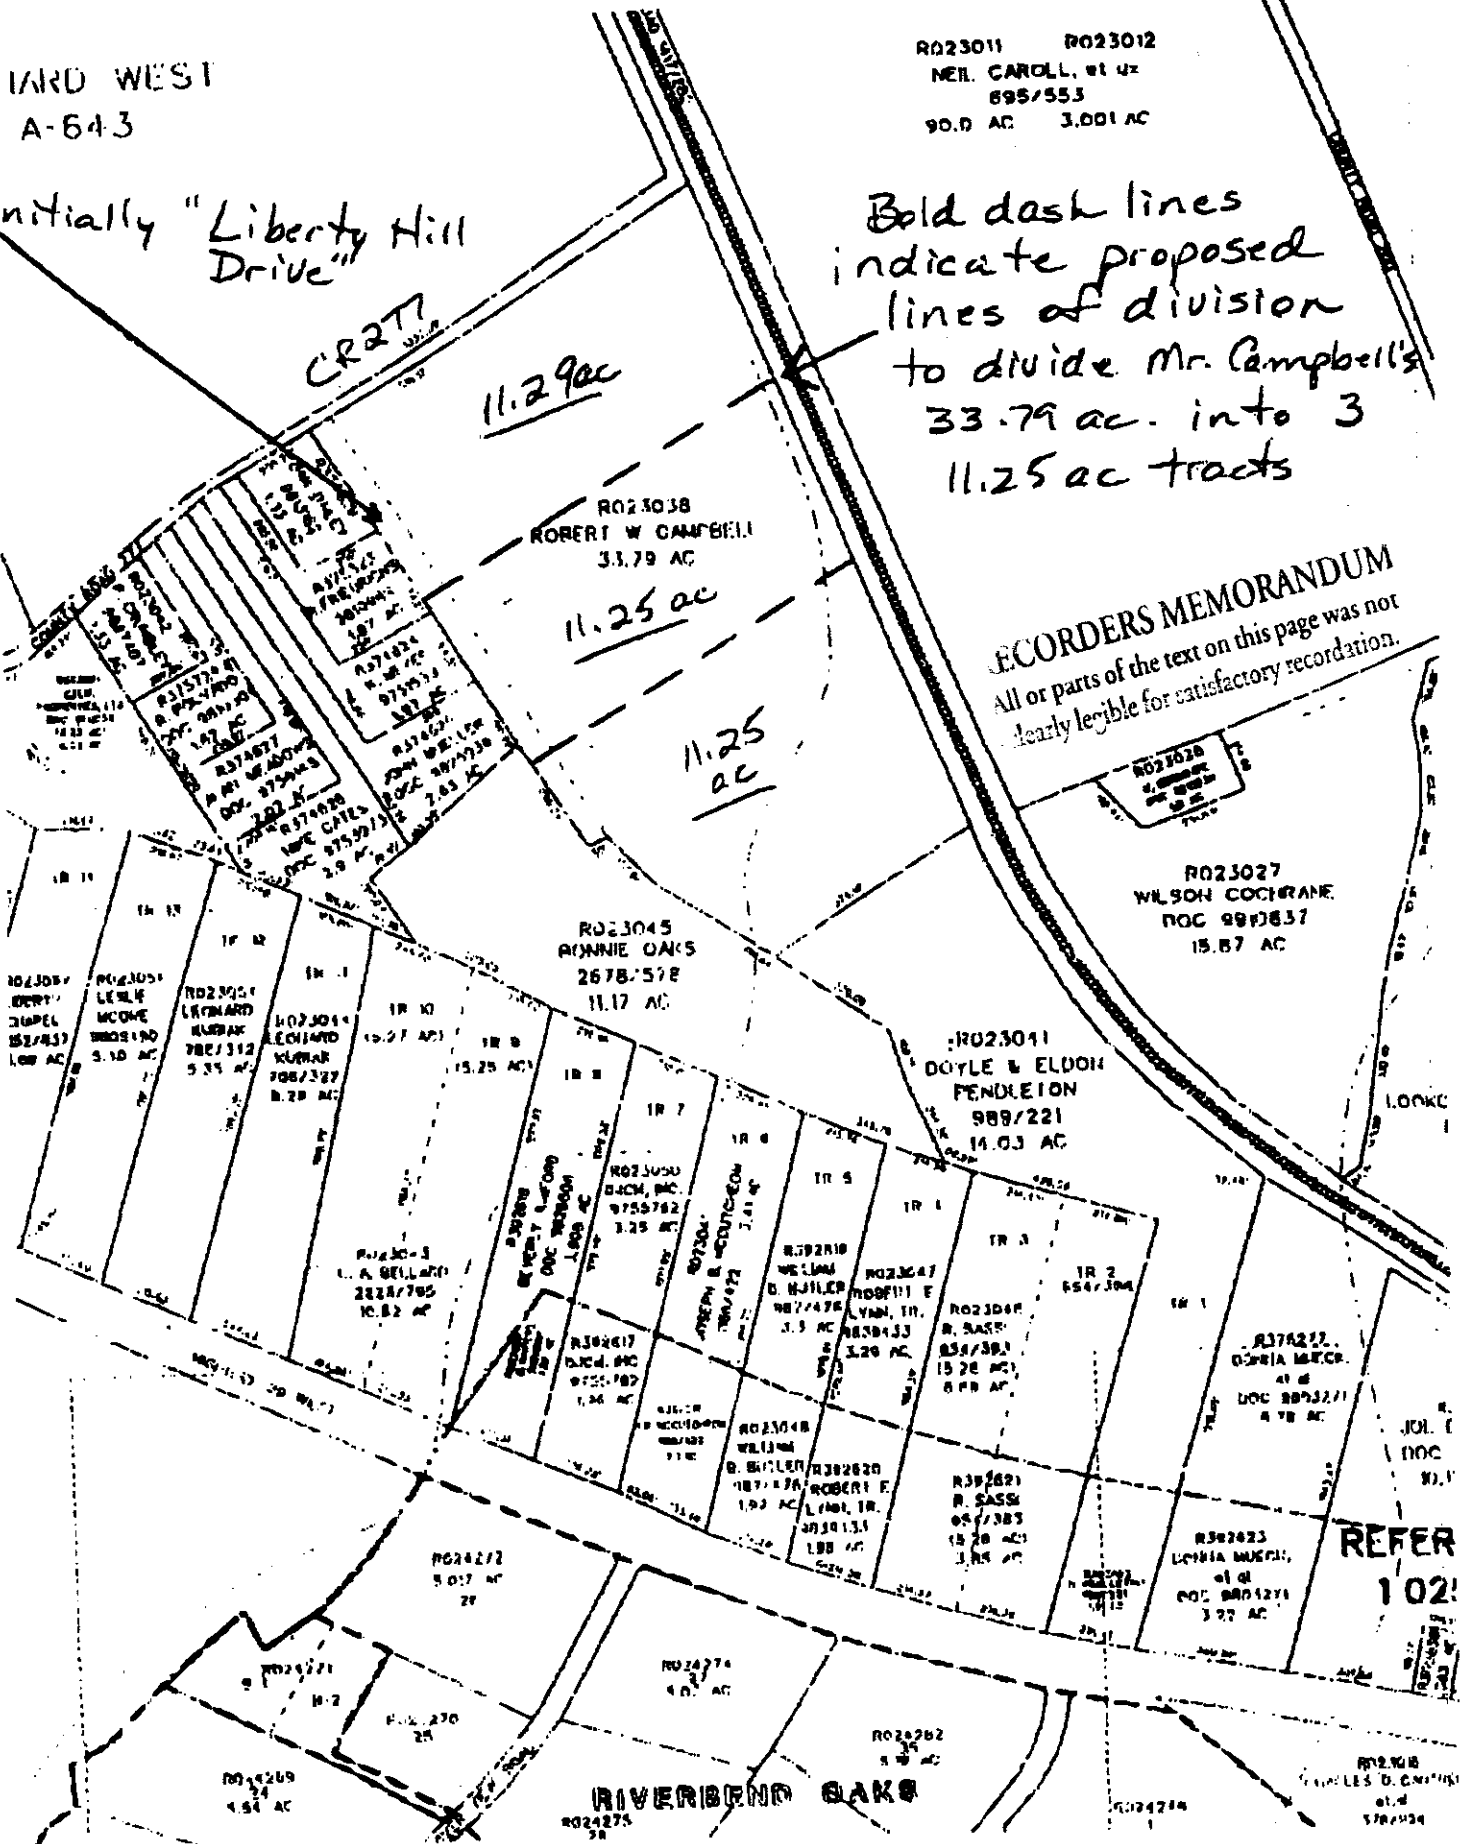

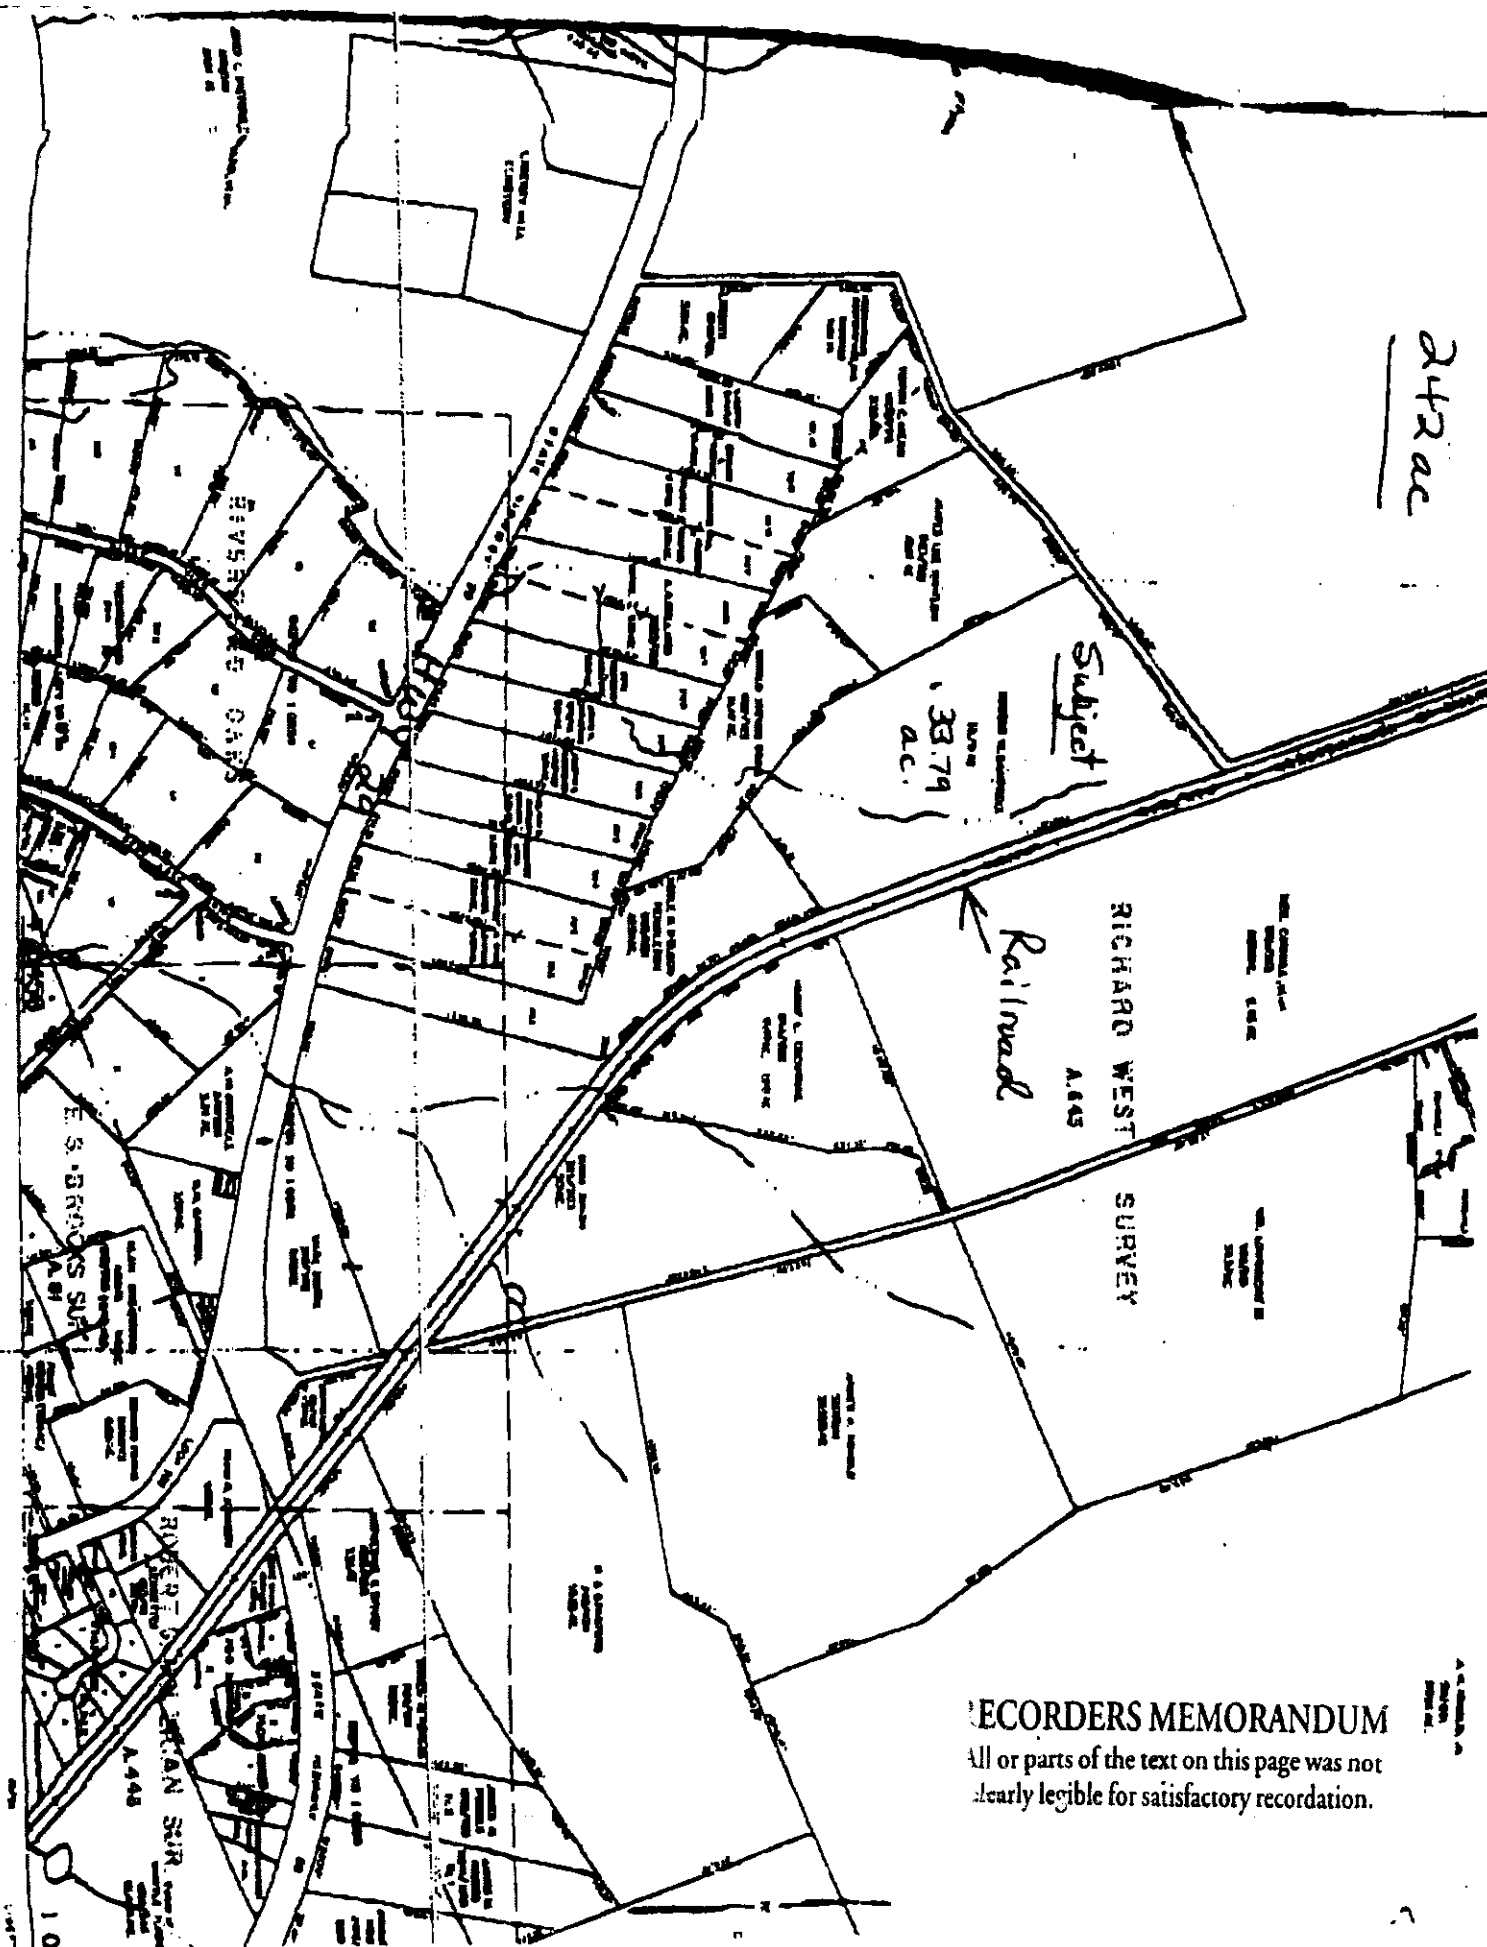

RECORDERS MEMORANDUM  
All or parts of the text on this page was not  
clearly legible for satisfactory recordation.

**AGENDA ITEM 21****Discuss and take appropriate action on road bond program.**

Road Bond Manager Mike Weaver discussed a presentation that was given to the Texas Transportation Commission on US 79, as well as the proposed RMA rules received from TxDOT. He stated that there will be a public hearing on the proposed RMA rules on February 27, 2002, regarding comments on the rules.

He suggested using County inspectors or hiring contract inspectors for some of the smaller road projects to save the County money while subdivision work is slow.

Mr. Weaver gave the court a schedule of road bond projects, and reported that the Texas Transportation Authority had postponed the SH 45 project until right-of-way issues are addressed.

Attorney Charlie Crossfield addressed the court concerning the status of right-of-way acquisition for SH 45.

Moved: **Commissioner Hays**

Seconded: **Commissioner Heiligenstein**

Motion: To schedule a work session for February 19, 2002 at 2:00 p.m.

Vote: **5 - 0**

***Copies of the Regional Mobility Authorities, Proposed Preamble and Proposed Rules and the Williamson County US 79 Presentation to Texas Transportation Commission are available for inspection in the County Clerk's office during normal business hours.***

< Attachment >

02/05/2002

PROJECT	Engineer	DESIGN		CONSTRUCTION (ORIGINAL)		CONSTRUCTION (REVISED)		PROGRESS - ACTION ITEMS - REMARKS
		START DATE	FINISH DATE	START DATE	FINISH DATE	START DATE	FINISH DATE	
Cedar Hollow at SH 29	Haynie	-	-	-	-	-	-	Project completed.
Chandler Road Phase I - (FM1460 - CR110) Phase II - (CR110 - FM1460)	Dennon	3/21/01 2/1/02	3/1/02 8/1/02	3/1/02 7/1/02	9/2/02 12/27/02	3/1/02 11/1/02	9/2/02 5/1/03	Phase I FM 1460 to CR 110 - 95% submittal early Feb. Dukette no longer with the firm, Kynn Cole is PM.
CR 137 (County Line to FM 1660)	Pate	6/18/01	4/4/02	9/2/02	7/1/03	9/2/02	7/1/03	County wants to hold another public meeting with property owners in the next 30 days. County wants the plans revised to require less cut north of the Brushy Creek Bridge. Work underway on drop structures within the ditch. County wants more information on the leach field that is shown to be in an area of cut south of the Brushy Creek Bridge. CFA reports the utilities in the ROW may, by law, be allowed to remain in the existing location. This may affect land swap on north end. HNTB to check with CFA, also Diamond about surveying progress.
CR 175 (FM 1431 to CR 176)	Baker-Aiklen	12/28/01	5/2/03	6/18/02	10/15/03	7/22/02	11/15/03	Design survey completed, ROW acquisition started and ROW staking completed. Engineering about 50%.
CR 200(CR 201 to Lackey Creek)	KC	12/10/01	6/28/02	10/1/02	1/31/03	10/2/02	2/3/03	PER to be completed by 2/15/02.
CR 214 (SH 29 to Rolling Hills Rd.)	Carter & Burgess	8/1/01	3/1/02	3/3/03	9/26/03	3/3/03	7/18/03	90% complete. On hold in design. Awaiting progress and coordination with Huggins-Seiler for the final alignment and profile of the tie-in with CR 214A project.
CR 214A (realignment at FM 1669)	Huggins - Seiler	12/17/01	7/17/02	2/3/03	8/4/03	2/3/03	8/4/03	On hold until signal issue resolved. Joe England & Huggins/Seiler to meet with Bubba Needham. Preferred alignment has been selected. Issue remains with a preference on ROW width (and curbed or shouldered section) for segment south of SH 29 intersection.
CR 276 (Parmer Lane to Bagdad Rd.)	Malone - Wheeler	5/1/01	8/22/02	6/3/02	3/3/03	10/2/02	7/9/03	On Schedule. Waiting on Malone/Wheeler report; 10% Preliminary Engineering Report
CR 300/CR 301 (FM 972 to FM 971)	Pate	12/4/01	4/6/02	7/1/02	5/1/03	7/24/02	12/10/02	Diamond Surveying submitting supplemental to cover metes and bounds survey on three additional parcels for drainage easements. Diamond currently performing the surveys for the northern 1-mile segment of project. Pate performing internal review of PER for CR 300/CR 326 "Y" intersection. Expects to have 60% plans complete by 2/15/03. Adding 300/326 "Y" intersection to the 300/301 plans.

02/05/2002

PROJECT	Engineer	DESIGN		CONSTRUCTION (ORIGINAL)		CONSTRUCTION (REVISED)		PROGRESS - ACTION ITEMS - REMARKS
		START DATE	FINISH DATE	START DATE	FINISH DATE	START DATE	FINISH DATE	
CR 368/369 (CR 101 to CR 366)	Haynie	3/5/01	12/28/01	1/15/02	7/1/02	3/4/02	8/16/02	Bid opening 2/14. Plans available 1/28. Haynie doing the Construction Observation.
CR 412 (FM 619 to CR 421)	Inland Civil	2/2/01	2/1/02	5/2/02	11/18/02	5/15/02	11/29/02	Will submit 70% plans in 2 weeks for review. The plans will include headwalls and stabilized slopes to eliminate need for additional ROW or easements.
Georgetown Inner Loop - FM 2338 to D.B. Woods (Project 1); Cedar Breaks	PBS&J	9/18/00	1/18/02	4/1/02	9/15/03	4/15/02	9/26/03	Advertisement date 2/11/02. No word yet from TNRCC on WPAP. Final comments on plan. Draft of specifications to HNTB on 2/4/02.
Georgetown Inner Loop - D.B. Woods Reconstruction - Middle Fork to SH 29 (Project 2)	PBS&J	9/1/00	10/31/02	11/18/01	7/1/02	1/23/02	10/1/02	NTP issued 1/23/02. ABR to begin construction survey, traffic control and erosion control work on 1/28/02. Heavy equipment to be mobilized 2/4/02.
Georgetown Inner Loop - SH 29 to FM 2243; D.B. Wood Reconstruction (Project 3)	Steger & Bizzell	2/2/01	1/2/02	2/1/02	4/2/03	TBA	TBA	ROW issues may be delayed.
Georgetown Inner Loop - FM 2243 to IH-35 (Project 4)	HDR	8/1/01	6/28/02	-	-	-	-	Developing preliminary horizontal alignment, reviewing traffic data and performing traffic analysis. Implemented TransCad program. No progress on environmental & public involvement.
Georgetown Inner Loop - 2338 to Shell Road; Shell Road Realignment (Project 5)	PBS&J		ON HOLD	-	-	-	-	Currently negotiating with property owners.
Georgetown Inner Loop (East) - SH 29 to FM 971 (Segment 2) FM 971 to IH 35	Steger & Bizzell	9/3/01	6/28/02	5/1/02	2/3/03	9/2/02	6/5/03	Received preliminary alignment on segment from SH 29 to FM 971. Reviewed alignment with Paulson for environmental constraints. WPAP will be needed. S&B is considering making the extension from FM 971 to IH 35 a separate drawing package.
Lakeline Blvd. (Lyndhurst to Parnet Lane)	Carter & Burgess	11/2/01	10/1/02	1/2/03	2/26/04	1/2/03	2/26/04	Awaiting owners to sign agreement for ROW donation. Meet with City of Austin on Thursday Feb 7. Contract being negotiated for work with the City of Austin

02/05/2002

PROJECT	Engineer	DESIGN		CONSTRUCTION (ORIGINAL)		CONSTRUCTION (REVISED)		PROGRESS - ACTION ITEMS - REMARKS
		START DATE	FINISH DATE	START DATE	FINISH DATE	START DATE	FINISH DATE	
McNeil Road (County Line/McNeil Cutoff to proposed SH 45)	Gray Jansing	4/3/01	7/1/02	8/1/02	2/2/04	8/1/02	2/2/04	Review of 30% plans completed, comments sent to Consultant. Hydraulic report comments being addressed. Awaiting decision on selected alignment in order to proceed. Need direction on how stormwater will be handled on Austin White Lime property (re: Round Rock stormwater detention).
Parmar Lane South (FM 1431 to FM 2243) (FM 2243 to SH 29)	TC&B	5/8/01	2/3/03 6/2/03	5/1/02 8/5/02	2/3/03 7/18/03	5/1/02 10/1/02	2/4/03 9/15/03	TC&B to prepare clearing and grubbing contract to start in May/June of 2002. Contract will be for entire project, special provisions will limit Contractor to entry to tracts outside the habitat area. Utility relocations to be performed by September. Start roadway construction thereafter. Schematic design is nearing completion on north segment.
Parmar Lane North (SH 29 to FM 2338)	PBS&J	3/26/01	12/31/02	3/3/03	9/3/04	3/3/03	9/3/04	Prepared list of stakeholders and exhibits for stakeholders meetings. Met with Geotech to discuss location of borings at bridge locations. Will coordinate with Geotech and Acl in field for final locations. WAFS approved in order to obtain survey in the bird habitat areas before March 1, 2002. Public meeting will be held sometime in March.
Pond Springs Road/Turtle Rock Road	WHM/ Huggins	11/6/01	3/1/02	11/6/01	3/1/02	1/3/02	4/30/02	Project under construction. Waiting on delivery of signal poles for installation - also final striping.
River Bend Oaks Subdivision	Haynie	5/2/01	11/9/01	1/8/02	4/4/02	3/1/02	5/14/02	Bid 1/17/02. 7 bidders responded - low bid \$440,000 - approx. \$10,000 under Engrs. Est. Haynie is doing the Construction Observation
SH 29 at FM 1869 (Traffic Signal)	Huggins - Seiler	3/2/01	12/20/01	4/1/02	7/12/02	5/1/02	8/20/02	Responding to TXDOT review comments.
US 79/CR 110 to Milam County Line) Section 1 (CR 100 to Hutto) Section 2 (Hutto to Taylor)	Carter & Burgess	4/9/01	2/3/03	3/14/2003 Subject to TXDOT funding	6/4/04	3/14/03	6/4/04	Section 1 - Revising schematic design to address review comments; will submit next week to HNTB & TXDOT. Section 2 - Schematic design will be submitted in 2 weeks. Continue to work on environmental document for all sections.
Wyoming Springs South (RM 620 to McNeil Road)	Baker-Aiken	2/1/02	6/27/02	3/13/03	3/24/04	3/13/03	3/24/04	4C funding (\$5.0 million) recommended by CAMPO. Preliminary survey and environmental is underway.
Wyoming Springs North (FM 1431 to Sam Bass Road/Brushy Creek)	Haynie	8/2/01	6/21/02	3/1/02	8/30/02	9/3/02	3/4/03	Working with landowners on ROW north of Sam Bass. Revising design contract to include Brushy Creek bridge.
